#	Task Name	Start	Duration
1	Site set out	4/5/21	1
2	Earthworks	14/5/21	3
3	Concrete steel	21/5/21	1
4	Retaining walls	25/5/21	1
5	Gravel and ground le	25/5/21	1
6	Timber delivery	31/5/21	1
7	Subfloor installation	1/6/21	2
8	Decking and posts	7/6/21	2
9	Frame out extension	8/6/21	3
10	Roof frame and shee	14/6/21	3
11	Kitchen Removal	16/6/21	3
12	Asbestos Removal	21/6/21	3
13	Internal framing	24/6/21	2
14	Plumbing Rough in	28/6/21	1
15	Electrical Rough in	28/6/21	4
16	External Cladding an	28/6/21	5
17	Cabinetry Measure u	2/7/21	1
18	Resheeting walls	2/7/21	1
19	Plastering	5/7/21	4
20	Waterproofing	5/7/21	2
21	Wet area tiling	7/7/21	4
22	Cabinetry Install	14/7/21	2
23	Stone measure up	15/7/21	1
24	Plumbing Fit off	14/7/21	3
25	Stone install	26/7/21	1
26	Electrical Fit off	27/7/21	1
27	Floor Sanding	29/7/21	2
28	Painting	19/7/21	5

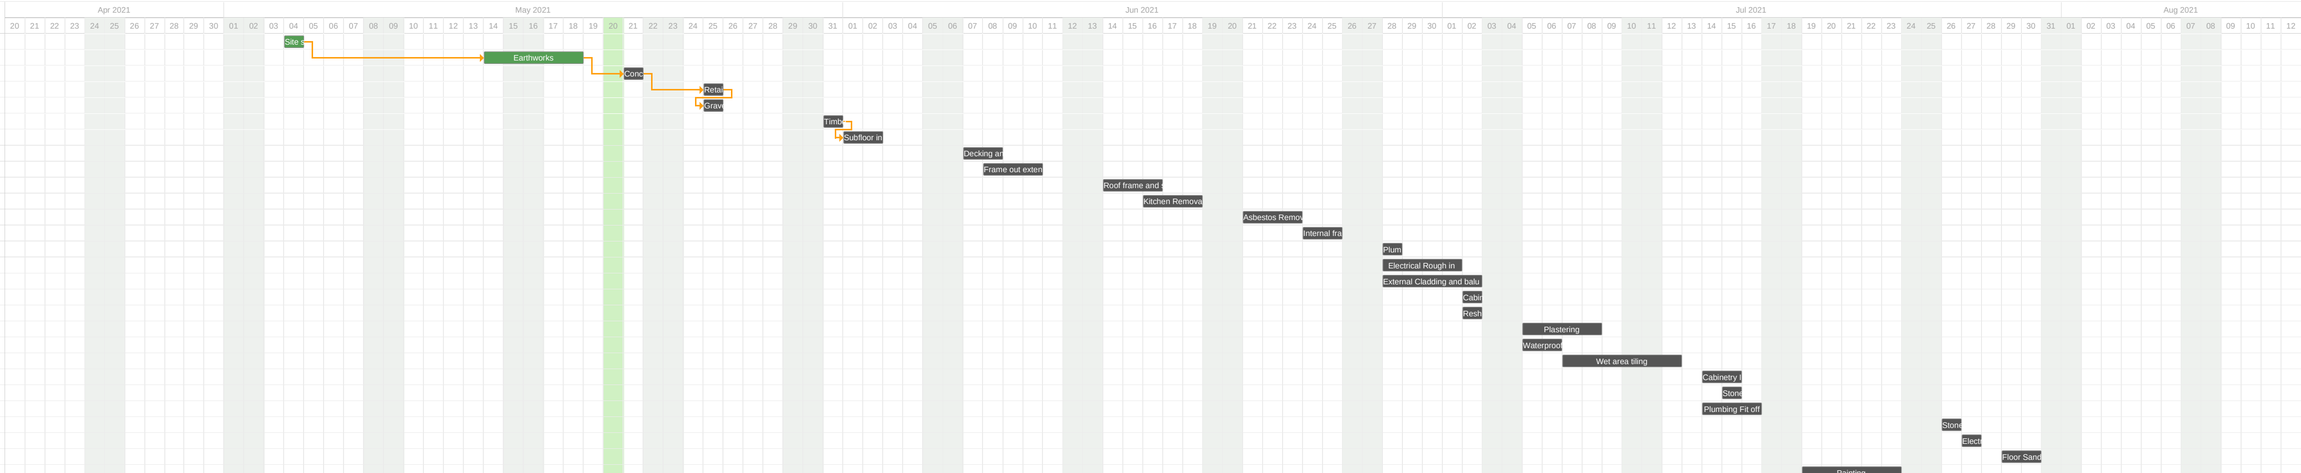

NB: Weekends are not included in the duration

This document is created with dhtmlx library: http://dhtmlx.com
